PALLAVI BOREWELL & DRILLERS

Dealers in : 6½" 4½" Borewells Drilling & Inwell Drilling
All Kinds of Motors & Pumps, Sales & Service
No. 66/8, 1st Main Road, Maruthi Layout, M. G. Road,
Nelamangala Bangalore - 562 123.
Moble : 93412 24311, 90089 87530,

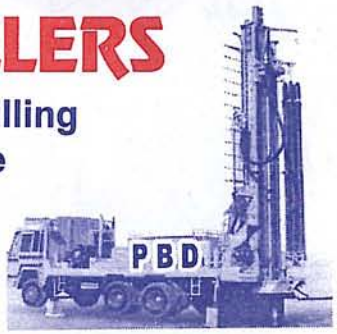

Ref : *Date :* 28.2.2014

YIELD REPORT

1. Name and Address of the Party : AEE Ward No 13 - Dasarahalli Sub Division BBMP
2. Borewell Location : Model Colony (Near Ramachandra Hospital)
3. Total Depth Drilled : 1147 Feet
4. Casing Pipe : 255 Feet
5. Coupling : 13 Collar's
6. Yield Details :
   a) First Spring Touched at : 495 Feet
   b) Second Spring Touched at : 860 Feet
   c) Third Spring Touched at : 957 Feet
7. Total Yield in G.P.H. : 1400 G.P.H
8. Remarks : Yield's Good

AE - 15

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಟಿ.ದಾಸರಹಳ್ಳಿ ಉಪ-ವಿಭಾಗ
ಬಾಗಲಗುಂಟೆ, ಬಿಬಿಎಂಪಿ
ಬೆಂಗಳೂರು

For PALLAVI BOREWELL & DRILLERS

M.B. Mallaiah

Proprietor

4th page : -2

A. N. CHOWDHARY, M.Sc.,
GEOLOGIST

Phone :
Cell : 98454 73398

SRI SHIRDI SAI CONSULTANTS

10, 3rd Floor, 19th Cross, 14th Main, Revenue Layout, Padamanabhanagar
Bangalore - 560 061.

GROUND WATER INVESTIGATION REPORT

To the Executive Engineer -
BBMP
Dasarahalli Sub Division
Off. Manthri Temple -
Bhuvaneshwarinagar -
Bangalore -

S. No. :

Date : 24.2.2014

1. Name of the Customer
2. a) Village ward no:- 15 3rd main b) Block / Taluk. c) District
3. Location.
4. Lithology of the Area — Granetic/Schistose in nature
5. Tophographic Features of the Area — The area was a plain land
6. Hydrogeological condition of the Area — Good -
7. Geophysical survey result. — By Diving method
   a) Type of Method.
   b) No of Soundings Conducted.
   c) Recommended Sounding.
   d) Particulars of formations present in the subsurface/possible ground water zones encountered at — Around 700' 960 - 990' 1100 - 1140' 2
   e) Condition of Ground Water. — Good
8. Type of well Recommended. — Bore well (6 1/2") -
9. Depth Recommended. — 1130 - 1160'
10. Expected Yield. — 1300 - 1500 GPH -
11. Quality of Water. — Good -
12. Approximate depth at which the water is expected to be met. — Around 700' -
13. Recommended Type and Length of casing to be inserted. — Around 160 - 190' of MS Casing may be needed - Strictly Advised -
14. Rain water Harvesting adviced or not — Recommended mainly for DWLP
15. Remarks.

Site Plan Map

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಟಿ.ದಾಸರಹಳ್ಳಿ ಉಪ-ವಿಭಾಗ
ದಾಸರಹಳ್ಳಿ ಬಿಬಿಎಂಪಿ
ಬೆಂಗಳೂರು

Signature of the consultant

Note :- The Survey was carried out by this divining / Geophysical method of surveying is with our good knowledge and experience. However no guarantee of water will be given.
